




# Project Status Update

**As of October 20th, 2025**

NVTA reports monthly the status of projects funded through the Regional Revenue (70%) Fund. Realtime updates can also be found on [Novagateway.org](https://www.novagateway.org)

# Project Status – Standard Project Agreements (SPAs)

There are a number of projects that received funding for different phases across various funding cycles. This results in the establishment of a SPA (Standard Project Agreement). The stages of a SPA are listed in 5 categories below. While there are a total of 179 SPAs across the different categories, these represent 135 unique projects.

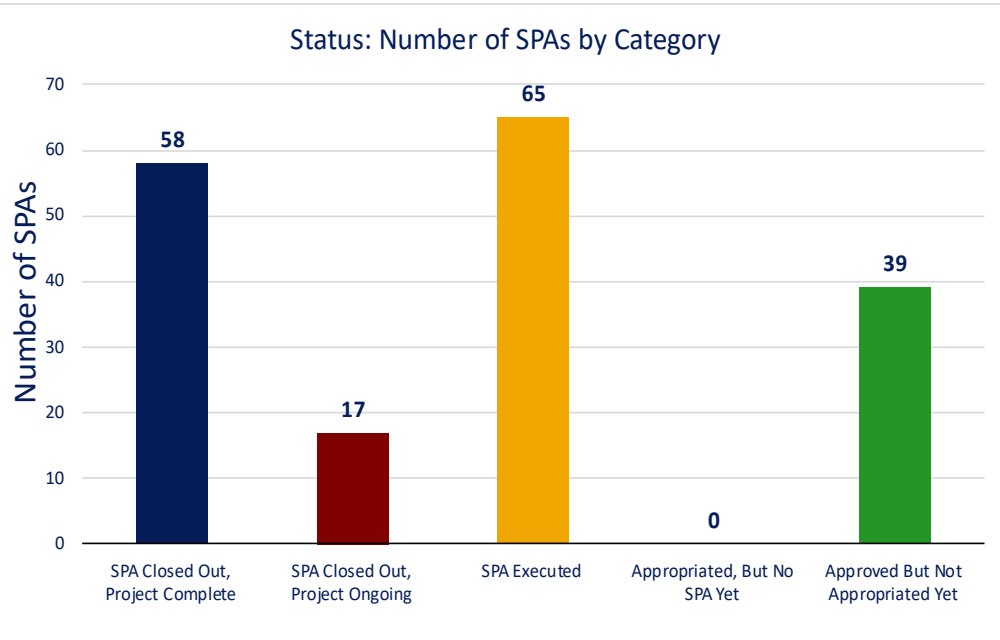

## 5 Classification Categories and Stages of a SPA


**SPA closed out, Project complete:** SPA has been closed out and NVTA funding has completed, and overall project has been completed.

**SPA closed out, Project ongoing:** SPA has been closed out and NVTA funding has completed. Overall project however, is still ongoing.

**SPA Executed:** SPA has been approved by NVTA.

**Appropriated but no SPA yet:** Funding allocation has been appropriated by NVTA, but SPA has not been executed yet. (Note: NVTA appropriates the total approved funding amount at time of appropriation)

**Approved but not appropriated yet:** Project Application approved by NVTA, but funding allocation has not been appropriated yet.

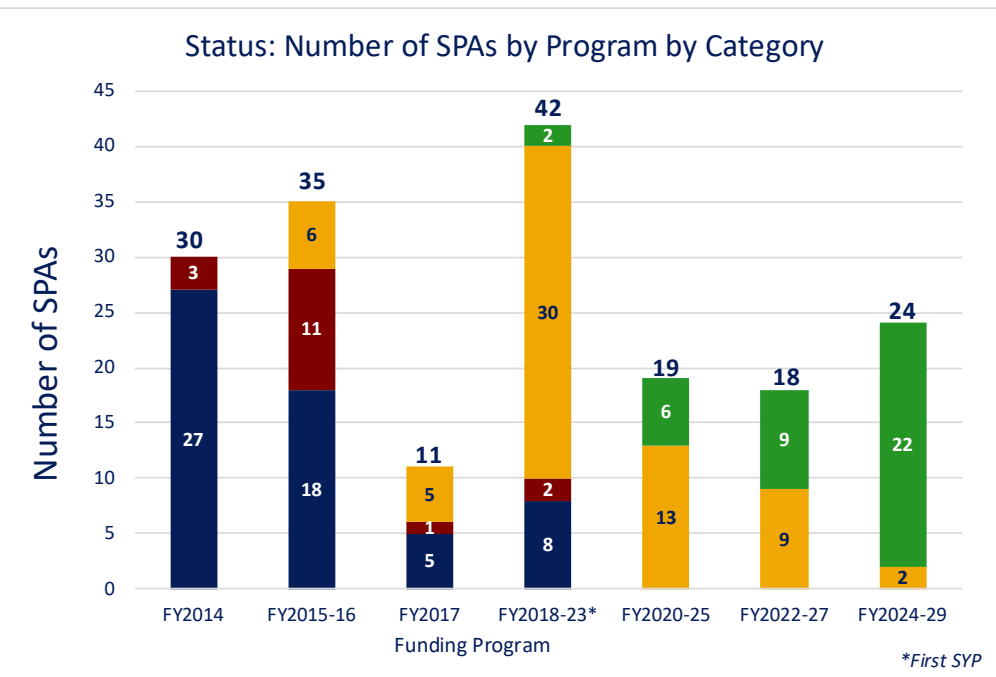


Note: NVTA's updates to the Six Year Program (SYP) allocate revenues from two future (outer) fiscal years (e.g., the FY2024-2029 SYP allocated funding for FY2028 and FY2029).

# Project Status – Revenue Approved, Appropriated and Reimbursed as of October 20th, 2025

NVTA has **approved** a total of: **\$3,683,182,918**

NVTA has **appropriated** a total of: **\$2,416,024,959**

NVTA has **reimbursed** a total of: **\$1,121,153,871**

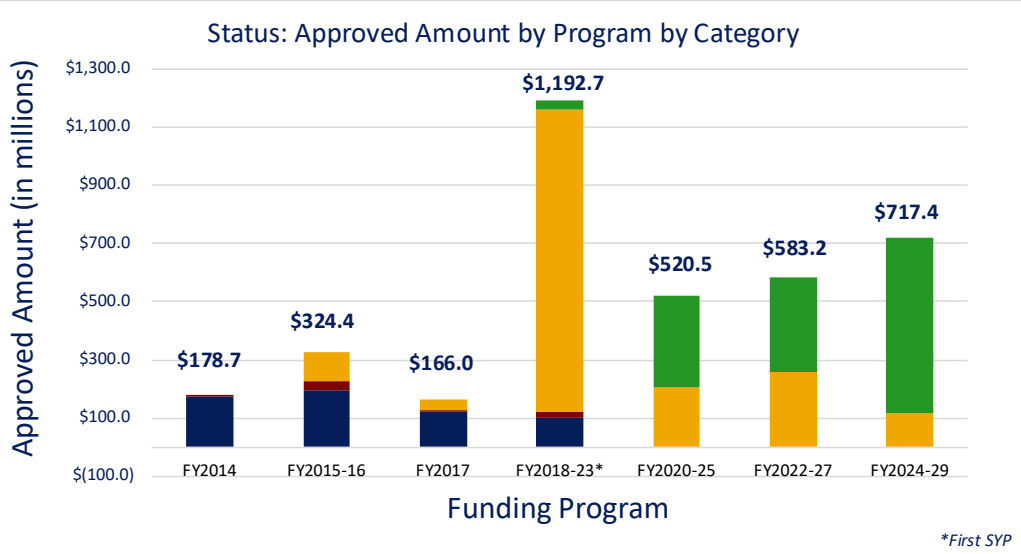

## 5 Classification Categories and Stages of a SPA


SPA closed out; Project complete

SPA closed out; Project ongoing

SPA Executed


Appropriated but no SPA yet

Approved but not appropriated yet

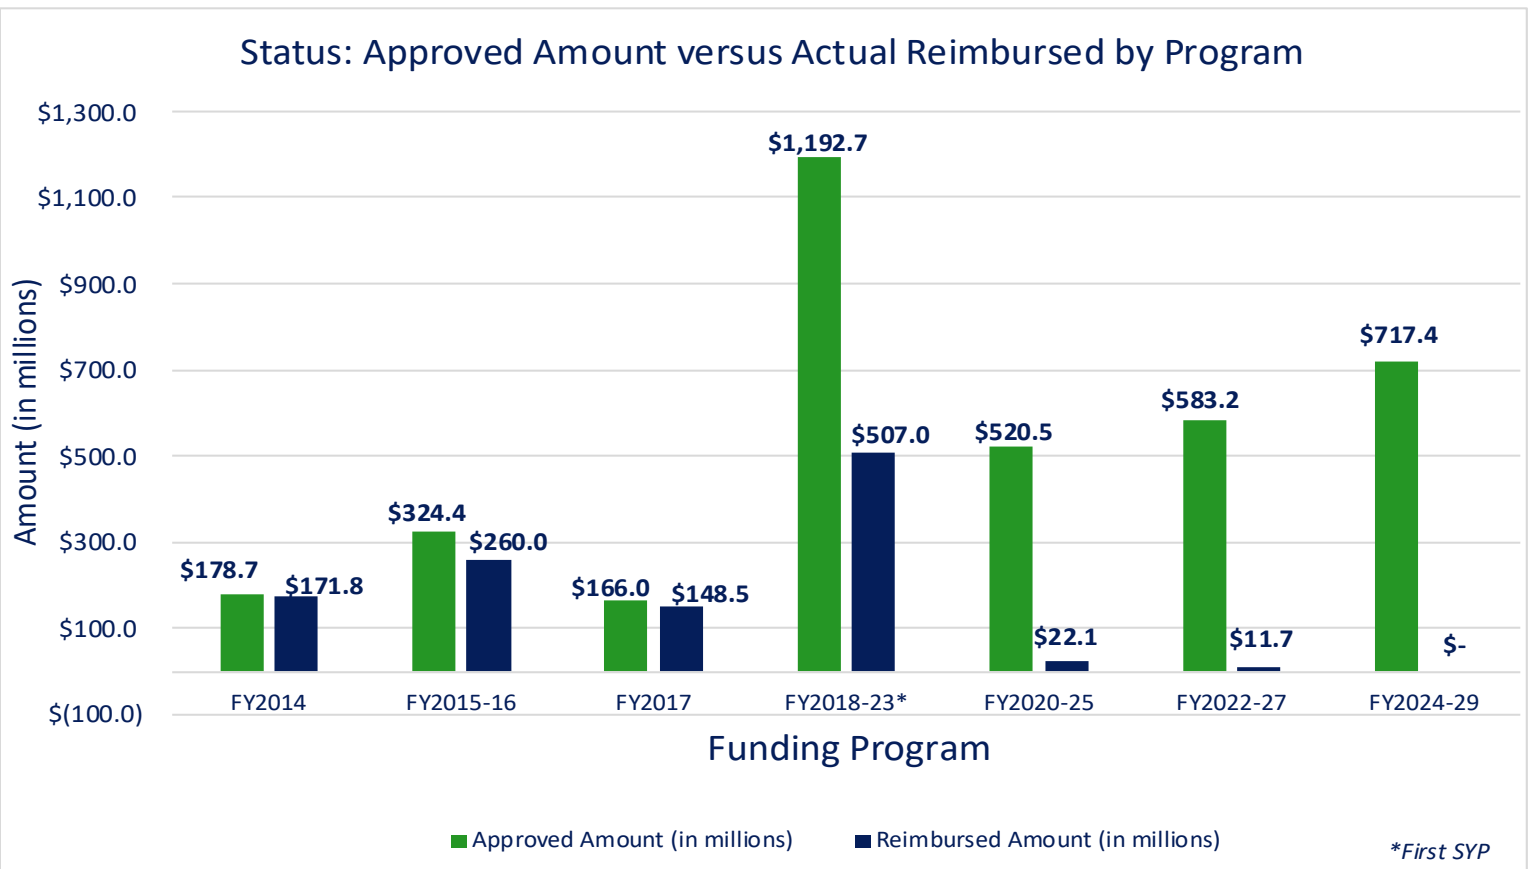

Note: SPAs usually request NVTA funds in the outer years of their approved funding period and then continue to drawdown into subsequent fiscal years. (e.g. SPAs in the FY2024-2029 SYP typically begin drawing funds by the end of FY2029, with most not fully utilizing their allocations until FY2032.)

# Recent Project Milestones



## VRE Manassas Park Station Parking Expansion

- October 21<sup>st</sup> Ribbon Cutting event held
- NVTA invested **\$2.5 million in Regional Revenue funds** toward the design of this project
  - Additionally, NVTA recommended **\$23.5 million** to the Commonwealth Transportation Board (CTB) through the I-66 Concessionaire Program toward this project




## Arlington County Army Navy Drive

- October 29<sup>th</sup> Ribbon Cutting event held
- Army Navy Drive is one portion of the overarching Pentagon City Multimodal Connections and Transitway Extension project, in which NVTA invested a total of **\$28.8 million in Regional Revenue funds**
  - In the Army Navy Drive portion, NVTA has invested **\$9.7 million**



# Recent Project Milestones *Continued*



## Alexandria DASH Facility

- October 30<sup>th</sup> Groundbreaking event held
- NVTa invested a total of **\$11.9 million in Regional Revenue funds** on this project
  - \$9.2 million toward eight new battery electric buses and \$2.7 million toward construction of the facility



# Substantive Project Status Updates

Substantive changes to SPAs for the period September 23<sup>rd</sup>, 2025- October 20<sup>th</sup>, 2025, are outlined below.

## SPAs Executed

- None

## Updated Funding Schedules

- Arlington County:
  - Intelligent Transportation System Improvements (2018-5-1)

## SPAs Closed Out

- None



# Substantive Project Status Updates *Continued*

Substantive updates reported by the project sponsor for the period of September 23<sup>rd</sup>, 2025, to October 20<sup>th</sup>, 2025, are outlined below.

*Substantive changes include but are not limited to project administration advancements, start/completion of phases, major engineering progress, project completion date changes, etc.*

Project Sponsor	Project Title	Updated Status	% Reimbursed (Program Year(s))
Arlington County	ART Operations and Maintenance Facilities	Project is currently awaiting Dominion Energy to install the transformer & meter for the Battery-electric bus equipment, which remains on back order. Given this, <b>the project completion timeline revised from 6/30/2025 to 3/31/2026.</b>	FY2018: 99%
Arlington County	Columbia Pike Multimodal Street Improvements - East	Utility companies continue to do work for cutover in preparation for the switch from above ground to underground utility service. <b>Completion pushed back one month to 11/31/2025.</b>	FY2015: 91%
Loudoun County	Dulles West Boulevard Widening: Loudoun County Parkway to Northstar Boulevard	Land acquisition and utility relocation activities continue. Land acquisition scheduled to complete December 2025. Construction Notice to Proceed is expected September 2026. <b>Project Completion date pushed from 6/30/2027 to 3/20/2028.</b>	FY2018: 11%
Loudoun County	Northstar Boulevard - Evergreen Mills Rd to Tall Cedars Parkway	<b>Project has achieved substantial completion.</b> The contractor is currently addressing punch list items and is also working on the VDOT street acceptance package.	FY2018: 75%
Loudoun County	Route 15 at Braddock Road Roundabout	After a 9-month hold on the project, Locally Administered Project (LAP) agreement has been completed. <b>Project completion date advanced from 8/17/2031 to 10/31/2029.</b>	FY2024: No SPA yet
City of Fairfax	Jermantown Road/Route 29 Intersection Improvements	<b>Preliminary Design settled.</b> Soil Investigation scheduled.	FY2020: 2%

# Substantive Project Status Updates *Continued*

## Flagged Projects – as of October 20<sup>th</sup> , 2025

Projects are flagged when there has been no update or no new information provided for three consecutive months.

Date of Last Update	Jurisdiction	Project Title	NVTA Funds	% Reimbursed
No new update since July 2025. Last update noted “ <i>Pre-construction meeting held 7/17/2025. NTP expected to be issued by end of the month</i> ”	ARL	Crystal City Streets: 12th Street Transitway	\$11,600,000	FY2017: 60%
No new update since June 2025. Last update noted “ <i>Under Active Construction.</i> ”	CFX	Government Center Parkway Extension	\$3,540,000	FY2020: 3%

## No Response Received This Cycle

Project sponsors are required to provide monthly updates on projects. NVTA did not receive a monthly update on the projects listed below.

- **Arlington County:** Crystal City Streets: 12th Street Transitway (FY2017), Intelligent Transportation System Improvements (FY2018-23) and Rosslyn Multimodal Network Improvements (FY2020-25)
- **VRE:** Franconia- Springfield Platform Improvements (FY2015), VRE Crystal City Station Improvements (FY2015/FY2018-23/FY2020-25)
